

AIA[®] Document A101[™] – 2007

Standard Form of Agreement Between Owner and Contractor where the basis of payment is a Stipulated Sum

A101-2007 v:1.0 (4-20-09) City

AGREEMENT made as of the day of April in the year 2010
(In words, indicate day, month and year)

BETWEEN the Owner:
(Name, address and other information)

City of Frisco
6101 Frisco Square Blvd.
5th Floor
Frisco, TX 75034

and the Contractor:
(Name, address and other information)

Primestar Construction
2952 Pinchurst
Cedar Hill, TX 75104
Telephone Number: 972-467-6762

for the following Project:
(Name, location and detailed description)

ARBJ File: Frisco 870008 0472 Park Contracts
(Preston Park North Renovation)
5400 Preston North Drive
Frisco, Texas 75035

Improvements to Preston Park North which include, but are not limited to, a new park shelter, children's playground, multi-use court, loop walk system, park ID signage, grading and drainage improvements, site furnishings, lighting, landscaping and irrigation.

The Architect:
(Name, address and other information)

Newman, Jackson, Beiberstein, Inc.
12770 Coit Road, Suite 210
Dallas, TX 75251

The Owner and Contractor agree as follows.

ADDITIONS AND DELETIONS:

The author of this document has added information needed for its completion. The author may also have revised the text of the original AIA standard form. An *Additions and Deletions Report* that notes added information as well as revisions to the standard form text is available from the author and should be reviewed. A vertical line in the left margin of this document indicates where the author has added necessary information and where the author has added to or deleted from the original AIA text.

This document has important legal consequences. Consultation with an attorney is encouraged with respect to its completion or modification.

AIA Document A201[™]-2007, General Conditions of the Contract for Construction, is adopted in this document by reference. Do not use with other general conditions unless this document is modified.

Int.

AIA Document A101[™] – 2007. Copyright © 1915, 1918, 1925, 1937, 1951, 1958, 1961, 1963, 1967, 1974, 1977, 1987, 1991, 1997 and 2007 by The American Institute of Architects. All rights reserved. WARNING: This AIA[®] Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA[®] Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law. This document was produced by AIA software at 09:50:01 on 04/01/2010 under Order No.8678215296_1 which expires on 06/11/2010, and is not for resale.
User Notes:

(812078409)

TABLE OF ARTICLES

- 1 THE CONTRACT DOCUMENTS
- 2 THE WORK OF THIS CONTRACT
- 3 DATE OF COMMENCEMENT AND SUBSTANTIAL COMPLETION
- 4 CONTRACT SUM
- 5 PAYMENTS
- 6 DISPUTE RESOLUTION
- 7 TERMINATION OR SUSPENSION
- 8 MISCELLANEOUS PROVISIONS
- 9 ENUMERATION OF CONTRACT DOCUMENTS
- 10 INSURANCE AND BONDS

ARTICLE 1 THE CONTRACT DOCUMENTS

The Contract Documents consist of this Agreement, Conditions of the Contract (General, Supplementary and other Conditions), Drawings, Specifications, Addenda issued prior to execution of this Agreement, other documents listed in this Agreement and Modifications issued after execution of this Agreement, all of which form the Contract, and are as fully a part of the Contract as if attached to this Agreement or repeated herein. The Contract represents the entire and integrated agreement between the parties hereto and supersedes prior negotiations, representations or agreements, either written or oral. An enumeration of the Contract Documents, other than a Modification, appears in Article 9.

ARTICLE 2 THE WORK OF THIS CONTRACT

The Contractor shall fully execute the Work described in the Contract Documents, except as specifically indicated in the Contract Documents to be the responsibility of others.

ARTICLE 3 DATE OF COMMENCEMENT AND SUBSTANTIAL COMPLETION

§ 3.1 The date of commencement of the Work shall be the date of this Agreement unless a different date is stated below or provision is made for the date to be fixed in a notice to proceed issued by the Owner.

(Insert the date of commencement if it differs from the date of this Agreement or, if applicable, state that the date will be fixed in a notice to proceed.)

The commencement date will be fixed in a notice to proceed.

If, prior to the commencement of the Work, the Owner requires time to file mortgages and other security interests, the Owner's time requirement shall be as follows:

§ 3.2 The Contract Time shall be measured from the date of commencement.

§ 3.3 The Contractor shall achieve Substantial Completion of the entire Work not later than 120 (120) calendar days from the date of commencement, or as follows:

(Insert number of calendar days. Alternatively, a calendar date may be used when coordinated with the date of commencement. If appropriate, insert requirements for earlier Substantial Completion of certain portions of the Work.)

Init.

Portion of Work

Substantial Completion Date

subject to adjustments of this Contract Time as provided in the Contract Documents.

(Insert provisions, if any, for liquidated damages relating to failure to achieve Substantial Completion on time or for bonus payments for early completion of the Work.)

Provisions are described in the A201 - 2007 v. 1.0 (4-14-09) Frisco, General Conditions of the Contract for Construction, provided by Owner, attached hereto and incorporated herein for all purposes.

ARTICLE 4. CONTRACT SUM

§ 4.1 The Owner shall pay the Contractor the Contract Sum in current funds for the Contractor's performance of the Contract. The Contract Sum shall be Three Hundred Thirteen Thousand Dollars (\$ 313,000.00), subject to additions and deductions as provided in the Contract Documents.

§ 4.2 The Contract Sum is based upon the following alternates, if any, which are described in the Contract Documents and are hereby accepted by the Owner:

(State the numbers or other identification of accepted alternates. If the bidding or proposal documents permit the Owner to accept other alternates subsequent to the execution of this Agreement, attach a schedule of such other alternates showing the amount for each and the date when that amount expires.)

None.

§ 4.3 Unit prices, if any: Unit prices as set forth in Exhibit "A" attached hereto and incorporated herein for all purposes.

(Identify and state the unit price; state quantity limitations, if any, to which the unit price will be applicable.)

Item	Units and Limitations	Price Per Unit
------	-----------------------	----------------

§ 4.4 Allowances included in the Contract Sum, if any: None.

(Identify allowance and state exclusions, if any, from the allowance price.)

Item	Price
------	-------

ARTICLE 5. PAYMENTS

§ 5.1. PROGRESS PAYMENTS

§ 5.1.1 Based upon Applications for Payment submitted to the Architect by the Contractor and Certificates for Payment issued by the Architect, the Owner shall make progress payments on account of the Contract Sum to the Contractor as provided below and elsewhere in the Contract Documents.

§ 5.1.2 The period covered by each Application for Payment shall be one calendar month ending on the last day of the month, or as follows:

§ 5.1.3 Provided that an Application for Payment is received by the Architect not later than the Fifth day of a month, the Owner shall make payment of the certified amount to the Contractor not later than the Twenty-fifth day of the following month. If an Application for Payment is received by the Architect after the application date fixed above, payment shall be made by the Owner not later than Twenty (20) days after the Architect receives the Application for Payment.

(Federal, state or local laws may require payment within a certain period of time.)

Init.

§ 5.1.4 Each Application for Payment shall be based on the most recent schedule of values submitted by the Contractor in accordance with the Contract Documents. The schedule of values shall allocate the entire Contract Sum among the various portions of the Work. The schedule of values shall be prepared in such form and supported by such data to substantiate its accuracy as the Architect may require. This schedule, unless objected to by the Architect, shall be used as a basis for reviewing the Contractor's Applications for Payment.

§ 5.1.5 Applications for Payment shall show the percentage of completion of each portion of the Work as of the end of the period covered by the Application for Payment.

§ 5.1.6 Subject to other provisions of the Contract Documents, the amount of each progress payment shall be computed as follows:

1. Take that portion of the Contract Sum properly allocable to completed Work as determined by multiplying the percentage completion of each portion of the Work by the share of the Contract Sum allocated to that portion of the Work in the schedule of values, less retainage of Five percent (5.00%); Pending final determination of cost to the Owner of changes in the Work, amounts not in dispute shall be included as provided in Section 7.3.9 of AIA Document A201™-2007, General Conditions of the Contract for Construction;
2. Add that portion of the Contract Sum properly allocable to materials and equipment delivered and suitably stored at the site for subsequent incorporation in the completed construction (or, if approved in advance by the Owner, suitably stored off the site at a location agreed upon in writing), less retainage of Five percent (5.00%);
3. Subtract the aggregate of previous payments made by the Owner; and
4. Subtract amounts, if any, for which the Architect has withheld or nullified a Certificate for Payment as provided in Section 9.5 of AIA Document A201-2007.

§ 5.1.7 The progress payment amount determined in accordance with Section 5.1.6 shall be further modified under the following circumstances:

1. Add, upon Substantial Completion of the Work, a sum sufficient to increase the total payments to the full amount of the Contract Sum, less such amounts as the Architect shall determine for incomplete Work; retainage applicable to such work and unsettled claims; and
(Section 9.8.5 of AIA Document A201-2007 requires release of applicable retainage upon Substantial Completion of Work with consent of surety, if any.)
2. Add, if final completion of the Work is thereafter materially delayed through no fault of the Contractor, any additional amounts payable in accordance with Section 9.10.3 of AIA Document A201-2007.

§ 5.1.8 Reduction or limitation of retainage, if any, shall be as follows:

(If it is intended, prior to Substantial Completion of the entire Work, to reduce or limit the retainage resulting from the percentages inserted in Sections 5.1.6.1 and 5.1.6.2 above, and this is not explained elsewhere in the Contract Documents, insert here provisions for such reduction or limitation.)

None.

§ 5.1.9 Except with the Owner's prior approval, the Contractor shall not make advance payments to suppliers for materials or equipment which have not been delivered and stored at the site.

§ 5.2 FINAL PAYMENT

§ 5.2.1 Final payment, constituting the entire unpaid balance of the Contract Sum, shall be made by the Owner to the Contractor when

1. the Contractor has fully performed the Contract except for the Contractor's responsibility to correct Work as provided in Section 12.2.2 of AIA Document A201-2007, and to satisfy other requirements, if any, which extend beyond final payment; and
2. a final Certificate for Payment has been issued by the Architect.

§ 5.2.2 The Owner's final payment to the Contractor shall be made no later than 30 days after the issuance of the Architect's final Certificate for Payment, or as follows:

init.

ARTICLE 6 DISPUTE RESOLUTION

§ 6.1 INITIAL DECISION MAKER

The Architect will serve as Initial Decision Maker pursuant to Section 15.2 of AIA Document A201-2007, unless the parties appoint below another individual, not a party to this Agreement, to serve as Initial Decision Maker.
(If the parties mutually agree, insert the name, address and other contact information of the Initial Decision Maker, if other than the Architect.)

§ 6.2 BINDING DISPUTE RESOLUTION

For any Claim subject to, but not resolved by, mediation pursuant to Section 15.3 of AIA Document A201-2007, the method of binding dispute resolution shall be as follows:

(Check the appropriate box. If the Owner and Contractor do not select a method of binding dispute resolution below, or do not subsequently agree in writing to a binding dispute resolution method other than litigation, Claims will be resolved by litigation in a court of competent jurisdiction.)

☐ Arbitration pursuant to Section 15.4 of AIA Document A201-2007

☒ Litigation in a court of competent jurisdiction

☐ Other *(Specify)*

ARTICLE 7 TERMINATION OR SUSPENSION

§ 7.1 The Contract may be terminated by the Owner or the Contractor as provided in Article 14 of AIA Document A201-2007.

§ 7.2 The Work may be suspended by the Owner as provided in Article 14 of AIA Document A201-2007.

ARTICLE 8 MISCELLANEOUS PROVISIONS

§ 8.1 Where reference is made in this Agreement to a provision of AIA Document A201-2007 or another Contract Document, the reference refers to that provision as amended or supplemented by other provisions of the Contract Documents.

§ 8.2 Payments due and unpaid under the Contract shall bear interest from the date payment is due at the rate stated below, or in the absence thereof, at the legal rate prevailing from time to time at the place where the Project is located.

(Insert rate of interest agreed upon, if any.)

The rate of interest computed in accordance with the provisions of Texas Government Code, Section 2251.025.

§ 8.3 The Owner's representative:

(Name, address and other information)

John E. Doshier
Parks Project Manager
6726 Walnut Street
Frisco, TX 75034
Telephone Number: 972-292-6514
jdoshier@frisco.texas.gov

§ 8.4 The Contractor's representative:

init.

AIA Document A101™ - 2007. Copyright © 1915, 1918, 1925, 1937, 1951, 1958, 1981, 1983, 1987, 1974, 1977, 1987, 1991, 1997 and 2007 by The American Institute of Architects. All rights reserved. WARNING: This AIA® Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA® Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law. This document was produced by AIA software at 09:50:01 on 04/01/2010 under Order No.8678216286_1 which expires on 09/11/2010, and is not for resale.
User Notes:

(812078409)

(Name, address and other information)

Felicia James
Primestar Construction
2952 Pinehurst
Cedar Hill, TX 75104
Telephone Number: 972-467-6762
fjames@primestarconstruction.com

§ 8.5 Neither the Owner's nor the Contractor's representative shall be changed without ten days written notice to the other party.

§ 8.6 Other provisions:

§ 8.6.1 CRIMINAL BACKGROUND Paragraph Intentionally Deleted.

§ 8.6.2 WORKING TIME AND WORKING RESTRICTIONS

§ 8.6.2.1 THE ENTIRE BUILDING IS TOBACCO-FREE AT ALL TIMES AND APPLIES TO ALL OCCUPANTS.

§ 8.6.2.2 Normal working hours and normal working days for Contractor's work on this Project shall be between 7:00 a.m. and 8:00 p.m., Monday through Friday, except as otherwise noted below. The Owner may require that certain limited portions of the Work be accomplished after normal working hours or other than on normal working days.

§ 8.6.2.3 Should Contractor desire to carry out portions of the Work at times other than between the hours and days stipulated above, he shall submit written request to do so to the Owner together with specific calendar days and hours he wishes to work and a description of the activities he proposes to carry out during those times. Construction activities will not be permitted at times other than those specified or subsequently approved in writing by the Owner. Only those activities specifically approved by Owner will be permitted during hours or on days other than those stipulated above.

§ 8.6.2.4 No extension of time will be granted and no "extra" or additional amount will be paid due to failure of Owner to approve performing of construction activities during hours other than those stipulated above.

§ 8.6.2.5 Work performed other than between 7:00 a.m. and 8:00 p.m., Monday through Friday, shall be done at no additional cost, whether work at other times is required by Owner or requested by Contractor and approved by Owner.

§ 8.6.2.6 If necessary in order to complete Work within time fixed in Contract or any extension thereof, Contractor shall request approval from Owner to perform work before 7:00 a.m. or after 8:00 p.m. or on weekends or holidays, and if Owner approves, shall perform work during such additional times and on such additional days as have been approved, at no additional cost to Owner. Work during such additional times and on such additional days shall continue only so long as is necessary to return work to on schedule or to complete the Work within the Contract Date.

ARTICLE 9 ENUMERATION OF CONTRACT DOCUMENTS

§ 9.1 The Contract Documents, except for Modifications issued after execution of this Agreement, are enumerated in the sections below.

§ 9.1.1 The Agreement is this executed AIA Document A101-2007, Standard Form of Agreement Between Owner and Contractor.

init

AIA Document A101™ - 2007. Copyright © 1915, 1918, 1925, 1937, 1951, 1958, 1981, 1983, 1987, 1974, 1977, 1987, 1991, 1997 and 2007 by The American Institute of Architects. All rights reserved. WARNING: This AIA® Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA® Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law. This document was produced by AIA software at 09:50:01 on 04/01/2010 under Order No.8678215298_1 which expires on 08/11/2010, and is not for resale.
User Notes:

(812078409)

§ 9.1.2 The General Conditions are AIA Document A201-2007 v: 1.0 (4-14-09) Frisco, General Conditions of the Contract for Construction provided by Owner.

§ 9.1.3 The Supplementary and other Conditions of the Contract:

Document	Title	Date	Pages
§ 9.1.4	The Specifications: Specifications as set forth in the City of Frisco Project Manual, Preston Park North, dated February 19, 2010, prepared by Newman, Jackson, Bieberstein, Inc., fully incorporated herein by reference. (Either list the Specifications here or refer to an exhibit attached to this Agreement.)		
	Title of Specifications exhibit: Exhibit B		

(Table deleted)

§ 9.1.5 The Drawings: All drawings referenced in the Index of Sheets set forth in Exhibit C, attached hereto and incorporated herein for all purposes. (Either list the Drawings here or refer to an exhibit attached to this Agreement.)

Title of Drawings exhibit: Article 9 (9.1.5) – The Drawings

(Table deleted)

§ 9.1.6 The Addenda, if any: As more fully set forth in Exhibit D, attached hereto and incorporated herein for all purposes.

Number	Date	Pages
Addendum No. 1	March 2, 2010	1-3

Portions of Addenda relating to bidding requirements are not part of the Contract Documents unless the bidding requirements are also enumerated in this Article 9.

§ 9.1.7 Additional documents, if any, forming part of the Contract Documents:

1. AIA Document E201™-2007, Digital Data Protocol Exhibit, if completed by the parties, or the following:
2. Other documents, if any, listed below:
(List here any additional documents that are intended to form part of the Contract Documents. AIA Document A201-2007 provides that bidding requirements such as advertisement or invitation to bid, Instructions to Bidders, sample forms and the Contractor's bid are not part of the Contract Documents unless enumerated in this Agreement. They should be listed here only if intended to be part of the Contract Documents.)
 1. Owner's Request for Proposal
 2. Contractor's Response to Request for Proposal

ARTICLE 10 INSURANCE AND BONDS

The Contractor shall purchase and maintain insurance and provide bonds as set forth in Article 11 of AIA Document A201-2007.

init.

This Agreement entered into as of the day and year first written above and is executed in at least three original copies, of which one is to be delivered to the Contractor, one to the Architect for use in the administration of the Contract, and the remainder to the Owner.

OWNER

City of Frisco, Texas

By: _____

(Printed name and title)

(Paragraphs deleted)

CONTRACTOR

Primestar Construction

By: _____

(Printed name and title)

Felicia James

Felicia James, President

Init.

AIA Document A101™ - 2007. Copyright © 1916, 1918, 1925, 1937, 1951, 1958, 1961, 1963, 1967, 1974, 1977, 1987, 1991, 1997 and 2007 by The American Institute of Architects. All rights reserved. WARNING: This AIA® Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA® Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law. This document was produced by AIA software at 09:50:01 on 04/01/2010 under Order No.8678215288_1 which expires on 06/11/2010, and is not for resale.
User Notes:

(812078403)

Additions and Deletions Report for AIA® Document A101™ – 2007

This Additions and Deletions Report, as defined on page 1 of the associated document, reproduces below all text the author has added to the standard form AIA document in order to complete it, as well as any text the author may have added to or deleted from the original AIA text. Added text is shown underlined. Deleted text is indicated with a horizontal line through the original AIA text.

Note: This Additions and Deletions Report is provided for information purposes only and is not incorporated into or constitute any part of the associated AIA document. This Additions and Deletions Report and its associated document were generated simultaneously by AIA software at 09:50:01 on 04/01/2010.

PAGE 1

A101-2007 v.1.0 (4-20-09) City

AGREEMENT made as of the day of April in the year 2010

...

(Name, legal status, address and other information)

City of Frisco
6101 Frisco Square Blvd.
5th Floor
Frisco, TX 75034

...

(Name, legal status, address and other information)

Primestar Construction
2952 Pinehurst
Cedar Hill, TX 75104
Telephone Number: 972-467-6762

...

(Name, location and detailed description)

ARBI File: Frisco 870008 0472 Park Contracts
(Preston Park North Renovation)
5400 Preston North Drive
Frisco, Texas 75035
Improvements to Preston Park North which include, but are not limited to, a new park shelter, children's playground, multi-use court, loop walk system, park ID signage, grading and drainage improvements, site furnishings, lighting, landscaping and irrigation.

...

(Name, legal status, address and other information)

Newman, Jackson, Beiberstein, Inc.
12770 Coit Road, Suite 210
Dallas, TX 75251

PAGE 2

The commencement date will be fixed in a notice to proceed.

§ 3.3 The Contractor shall achieve Substantial Completion of the entire Work not later than 120 (120) calendar days from the date of commencement, or as follows:

PAGE 3

Provisions are described in the A201 - 2007 v: 1.0 (4-14-09) Frisco, General Conditions of the Contract for Construction; provided by Owner, attached hereto and incorporated herein for all purposes.

§ 4.1 The Owner shall pay the Contractor the Contract Sum in current funds for the Contractor's performance of the Contract. The Contract Sum shall be Three Hundred Thirteen Thousand Dollars (\$ 313,000.00), subject to additions and deductions as provided in the Contract Documents.

None.

§ 4.3 Unit prices, if any: Unit prices as set forth in Exhibit "A" attached hereto and incorporated herein for all purposes.

Item	Units and Limitations	Price Per Unit(\$0.00)
§ 4.4 Allowances included in the Contract Sum, if any: <u>None.</u>		

§ 5.1.3 Provided that an Application for Payment is received by the Architect not later than the Fifth day of a month, the Owner shall make payment of the certified amount to the Contractor not later than the Twenty-fifth day of the following month. If an Application for Payment is received by the Architect after the application date fixed above, payment shall be made by the Owner not later than Twenty (20) days after the Architect receives the Application for Payment.

PAGE 4

1. Take that portion of the Contract Sum properly allocable to completed Work as determined by multiplying the percentage completion of each portion of the Work by the share of the Contract Sum allocated to that portion of the Work in the schedule of values, less retainage of Five percent (5.00%). Pending final determination of cost to the Owner of changes in the Work, amounts not in dispute shall be included as provided in Section 7.3.9 of AIA Document A201™-2007, General Conditions of the Contract for Construction;
2. Add that portion of the Contract Sum properly allocable to materials and equipment delivered and suitably stored at the site for subsequent incorporation in the completed construction (or, if approved in advance by the Owner, suitably stored off the site at a location agreed upon in writing), less retainage of Five percent (5.00%);

None.

PAGE 5

[X] Litigation in a court of competent jurisdiction

The rate of interest computed in accordance with the provisions of Texas Government Code, Section 2251.025.

John E. Doshier
Parks Project Manager
6726 Walnut Street
Frisco, TX 75034
Telephone Number: 972-292-6514
jdoshier@friscotexas.gov

PAGE 6

Felicia James
Primestar Construction
2952 Pinelhurst
Cedar Hill, TX 75104
Telephone Number: 972-467-6762
fjames@primestarcconstruction.com

§8.6.1 CRIMINAL BACKGROUND Paragraph Intentionally Deleted.

§8.6.2 WORKING TIME AND WORKING RESTRICTIONS

§8.6.2.1 THE ENTIRE BUILDING IS TOBACCO-FREE AT ALL TIMES AND APPLIES TO ALL OCCUPANTS.

§8.6.2.2 Normal working hours and normal working days for Contractor's work on this Project shall be between 7:00 a.m. and 8:00 p.m., Monday through Friday, except as otherwise noted below. The Owner may require that certain limited portions of the Work be accomplished after normal working hours or other than on normal working days.

§8.6.2.3 Should Contractor desire to carry out portions of the Work at times other than between the hours and days stipulated above, he shall submit written request to do so to the Owner together with specific calendar days and hours he wishes to work and a description of the activities he proposes to carry out during those times. Construction activities will not be permitted at times other than those specified or subsequently approved in writing by the Owner. Only those activities specifically approved by Owner will be permitted during hours or on days other than those stipulated above.

§8.6.2.4 No extension of time will be granted and no "extra" or additional amount will be paid due to failure of Owner to approve performing of construction activities during hours other than those stipulated above.

§8.6.2.5 Work performed other than between 7:00 a.m. and 8:00 p.m., Monday through Friday, shall be done at no additional cost whether work at other times is required by Owner or requested by Contractor and approved by Owner.

§8.6.2.6 If necessary in order to complete Work within time fixed in Contract or any extension thereof, Contractor shall request approval from Owner to perform work before 7:00 a.m. or after 8:00 p.m. or on weekends or holidays, and if Owner approves, shall perform work during such additional times and on such additional days as have been approved, at no additional cost to Owner. Work during such additional times and on such additional days shall

continue only so long as is necessary to return work to on schedule or to complete the Work within the Contract Date.

PAGE 7

§ 9.1.2 The General Conditions are AIA Document A201-2007, A201-2007 v: 1.0 (4-14-09) Frisco, General Conditions of the Contract for Construction, Construction provided by Owner.

§ 9.1.4 The Specifications: Specifications as set forth in the City of Frisco Project Manual, Preston Park North, dated February 19, 2010, prepared by Newman, Jackson, Bieberstein, Inc., fully incorporated herein by reference.

Title of Specifications exhibit: Exhibit B

Section	Title	Date	Pages
---------	-------	------	-------

§ 9.1.5 The Drawings: All drawings referenced in the Index of Sheets set forth in Exhibit C, attached hereto and incorporated herein for all purposes.

Title of Drawings exhibit: Article 9 (9.1.5) – The Drawings

Number	Title	Date
--------	-------	------

§ 9.1.6 The Addenda, if any: As more fully set forth in Exhibit D, attached hereto and incorporated herein for all purposes.

<u>Addendum No. 1</u>	<u>March 2, 2010</u>	<u>1-3</u>
-----------------------	----------------------	------------

1. Owner's Request for Proposal
2. Contractor's Response to Request for Proposal

(State bonding requirements, if any,

and limits of liability for insurance required in Article 11 of AIA Document A201-2007.)

This Agreement entered into as of the day and year first written above and is executed in at least three original copies, of which one is to be delivered to the Contractor, one to the Architect for use in the administration of the Contract, and the remainder to the Owner.

Type of insurance or bond

Limit of liability or bond amount (\$0.00)

OWNER

City of Frisco, Texas

By:

(Printed name and title)

This Agreement entered into as of the day and year first written above.

OWNER (Signature)

(Printed name and title)

CONTRACTOR

Primestar Construction

By:

Felicia James, President

(Printed name and title)

CONTRACTOR (Signature)

(Printed name and title)

Certification of Document's Authenticity

AIA® Document D401™ – 2003

I, hereby certify, to the best of my knowledge, information and belief, that I created the attached final document simultaneously with its associated Additions and Deletions Report and this certification at 09:50:01 on 04/01/2010 under Order No. 8678215296_1 from AIA Contract Documents software and that in preparing the attached final document I made no changes to the original text of AIA® Document A101™ – 2007 - Standard Form of Agreement Between Owner and Contractor where the basis of payment is a Stipulated Sum, as published by the AIA in its software, other than those additions and deletions shown in the associated Additions and Deletions Report.


(Signed)

(Title)

(Dated)

Exhibit A

SECTION 00400 - BID FORM

DALLAS, Texas

3/8/, 2000

PROPOSAL OF PRIMESTAR Development Corporation dba PRIMESTAR CORP A Corporation
organized and existing under the laws of the State of TEXAS
a partnership consisting of _____
the business name of _____, an
individual.

TO: THE CITY OF FRISCO, TEXAS

PROPOSAL FOR: PRESTON PARK NORTH AND CORRIDOR
(Bid No. 1002-033)

The undersigned Bidder has carefully examined the Advertisement for Bids, Instructions to Bidders, this Proposal, the Supplementary Conditions, the form of Contract Agreement and Bonds, the General Conditions of the Agreement, the Specifications, the Drawings, and the site of the work, and will provide all necessary labor, superintendence, machinery, equipment, tools, materials, services and other facilities to complete fully all the work as provided in the Contract Documents; and will execute the contract and bonds in the Contract Documents upon formal acceptance of this Proposal for the following prices:

BASE BID (Including allowances):

Three Hundred Thirteen thousand and zero
cents dollars, (\$ 313,000.00).

(NOTE: Show amounts in both written and figure form. In case of discrepancy between the written amount and the figure amount, the written amounts govern).

PROJECT COST BREAKDOWN:

Please provide a Base Bid breakdown into the following components. The totals for each of the items listed below should equal the Base Bid:

A.	Preston Park North	\$ - 288,000.00	dollars
1.	Electrical connection allowance	\$ 10,000	dollars
2.	Contingency allowance	\$ 15,000	dollars

TOTAL PROJECT COST (must equal Base Bid):

Three Hundred thirteen thousand and
zero cents dollars, (\$ 313,000.00).

UNIT PRICES

After the award of the Contract and in the event a greater or lesser amount of work is done, the following unit prices will apply. Unit prices cover the cost of the work and materials in place, including materials, equipment, labor, taxes, overhead, profit, maintenance and guarantee required to render the same complete.

A.	<u>Construction Items</u>	<u>Price</u>
1.	Concrete walk (4", 3500 PSI)	\$ 3.15 per sq. yd.
2.	Integral 6" concrete curb	\$ 9.75 per lin. ft.
3.	Concrete Mow Strips	\$ 18.75 per lin. ft.
4.	Earthwork - cut	\$ 2.25 per cu. yd.
5.	Earthwork - on-site fill	\$ 2.25 per cu. yd.
6.	Earthwork - imported topsoil fill	\$ 12.75 per cu. yd.
7.	6' ht. Orn. Metal Fence	\$ 34.00 per lin. ft.
8.	Light fixture (Type A, per fix. Sch. E2)	\$ 4500.00 each
9.	Light fixture (Type B, per fix. Sch. E2)	\$ 300.00 each
10.	6" Solid Drain Pipe	\$ 7.50 per lin. ft.
11.	4" Slotted Drain Pipe	\$ 16.00 per lin. ft.
12.	Prefabricated shelter	\$ 18,000.00 each
13.	Stone Columns	\$ 1,800.00 each
14.	Park benches	\$ 1,200.00 each
15.	Silt fencing	\$ 1.05 per sq.
16.	Picnic tables:	
a.	Square	\$ 1500.00 each
b.	ADA Accessible	\$ 1,350.00 each
17.	Drinking fountain	\$ 5000.00 each
18.	Bike Rack	\$ 120.00 each
19.	Park entry sign	\$ 10,500.00 each
20.	Basketball court with striping	\$ 12,500.00 per lin. ft.
21.	Playground Equipment	\$ 63,000.00 each
22.	Engineered wood fiber playground surface	\$ 28.00 per cu. yd.
23.	Drainage Culvert	\$ 2,000.00 each
24.	River Rock on Concrete	\$ 35.00 per sq ft.

B. Planting

1.	Hydromulch Bermudagrass	\$.06	per sq. ft.
2.	Solid sod Bermudagrass	\$.23	per sq. ft.
3.	Eldarica Pine (30 gal.)	\$	350. ⁰⁰	each
4.	Chinese Pistache (65 gal.)	\$	280. ⁰⁰	each
5.	Live Oak (65 gal.)	\$	350. ⁰⁰	each
6.	Red Bud (30 gal.)	\$	250. ⁰⁰	each
7.	Nellie R. Stevens (7 gal.)	\$	25. ⁰⁰	each
8.	Shumard Oak (65 gal.)	\$	350. ⁰⁰	each
9.	Vitex (30 gal.)	\$	250. ⁰⁰	each
10.	Liriope (4" pot)	\$	1. ⁰⁰	each
11.	Crapemyrtle (30 gal.)	\$	250. ⁰⁰	each
12.	Dwf. Pampass Grass (5 gal.)	\$	20. ⁰⁰	each

C. Irrigation

1.	Lawn spray head	\$	4.54	each
2.	High-pop spray head	\$	17.56	each
3.	Bubbler head	\$	5.50	each
4.	Rotary head	\$	49.80	each
5.	Spray head	\$	17.56	each
6.	Remote control valve w/ ball valve (1")	\$	125. ⁰⁰	each
7.	Remote control valve w/ ball valve (1-1/2")	\$	137. ⁰⁰	each
8.	Remote control valve w/ ball valve (2")	\$	190. ⁰⁰	each
9.	Gate valve (2-1/2")	\$	150. ⁰⁰	each
10.	Quick coupling valve (3/4")	\$	111. ⁰⁰	each
11.	Freeze sensor	\$	34. ⁰⁰	each
12.	Rain sensor	\$	31. ⁰⁰	each
13.	Controller (48 sta)	\$	NT	each
14.	Temporary Controller (24 sta)	\$	425. ⁰⁰	each
15.	Water meter (2")	\$		each
16.	Backflow preventor (2")	\$	700. ⁰⁰	each
17.	Hydrometer (2")	\$	200. ⁰⁰	each

SUBCONTRACTS:

The undersigned will enter into contract with the following subcontractor(s) subject to the approval of the Owner.

Contractor:

For installation of:

Preston Park North
NJB Project No. 0009-09

00400-3

Exhibit B



CITY OF FRISCO

Project Manual

Preston Park North

City of Frisco
Parks & Recreation Department
February 19, 2010
Bid No. 1002-033

NEWMAN, JACKSON, EIBERSTEIN, INC.
Landscape Architecture / Urban Design
Dallas, Texas




EXHIBIT 'B'

Preston Park North Estates Project Manual – Table of Contents

(SPECIFICATION SECTIONS PROVIDED BY NEWMAN, JACKSON, BIEBERSTEIN, INC.
UNLESS OTHERWISE *NOTED)

<u>Information Available to Bidders</u>	<u>No. of Pages</u>
Soil Investigation Data	24
 <u>Bidding Requirements</u>	
00100 Advertisement for Bids	1
00200 Instructions to Bidders	5
General Information	18
Wage Rates	1
00400 Bid Form	6
 <u>Contract Requirements</u>	
00500 Agreement	1
00600 Bonds	7
00700 General Conditions of the Contract for Construction	1
AIA Document A201-2007	81
00800 Supplementary Conditions to the Contract for Construction	26
 <u>Division 1 – General Requirements</u>	
01020 – Allowances	1
01100 – Summary of Work	2
01295 – Schedule of Values	2
01314 – Project Meetings	3
01320 – Construction Progress Documentation	2
01330 – Submittal Procedures	3
01450 – Quality Control	3
01451 – Testing Laboratory Services	3
01500 – Temporary Facilities and Controls	4
01560 – Tree Protection	3
01580 – Project Identification and Signs	2
01600 – Product Requirements	5
01700 – Project Execution Requirements	2
01770 – Contract Closeout	4
 <u>Division 2 – Site Construction</u>	
*02100 – Site Preparation (provided by Metropolitan Infrastructure)	3
*02270 – Soil Erosion and Sediment Control (provided by Metropolitan Infrastructure)	3
*02300 – Earth Work and Site Grading (provided by Metropolitan Infrastructure)	5
*02520 – Portland Cement Concrete Walks and Paving	6
02600 – Drainage System (provided by Metropolitan Infrastructure)	3
02780 – Unit Pavers	6

Preston Park North
NJB Project No. 0009-09

TOC-1

EXHIBIT 'B'

*02810 – Irrigation System	8
02820 – Fences	3
02850 – Prefabricated Shelter	2
02870 – Site Furnishings	2
02880 – Playground and Multi-use Court Equipment and Structures	4
02900 – Planting	8
02920 – Lawns and Grass	4

Division 3 – Concrete

*03100 – Concrete Formwork (provided by Metropolitan Infrastructure)	3
*03200 – Concrete Reinforcement and Embed Metal Assemblies (provided by Metropolitan Infrastructure)	5
*03300 – Cast-in-Place Concrete (provided by Metropolitan Infrastructure)	6
03314 – Post-Tension of Concrete (provided by Metropolitan Infrastructure)	9

Division 4 – Masonry

04100 – Mortar and Masonry Grout	4
04451 – Stone Work	3

Division 5 – Metals

05720 – Metal Fabrications	3
----------------------------	---

Division 6 – Wood and Plastics – Not Used

Division 7 – Thermal and Moisture Protection

07180 – Water Repellents	3
07920 – Site Joint Sealants	6

Division 8 – Doors and Windows – Not Used

Division 9 – Finishes

09900 – Painting	5
------------------	---

Division 10 – Specialties – Not Used

Division 11 – Equipment – Not Used

Division 12 – Furnishings – Not Used

Division 13 – Special Construction – Not Used

Division 14 – Conveying Equipment – Not Used

Division 15 – Mechanical – Not Used

Division 16 – Electrical – Not Used

Preston Park North
NJB Project No. 0809-09

TOC-2

Exhibit 'C'

Article 9 (9.1.5) – The Drawings:

All drawings referenced in the Index of Sheets attached hereto as

SHEET L1.0 ... DEMO PLAN
SHEET L2.0 ...LAYOUT PLAN
SHEET L3.0 ...PLANTING PLAN
SHEET L4.0 ...DETAILS
SHEET L5.0 ...DETAILS
SHEET L6.0 ...DETAILS
SHEET L7.0 ...DETAILS
SHEET L7.1 ...IRRIGATION PLAN
SHEET L7.2 ...DETAIL PLAN
SHEET C1.0 ...GRADING PLAN
SHEET C1.1 ...WATER UTILITY PLAN
SHEET C2.0 ...DRAINAGE PLAN
SHEET C3.0 ...FOUNDATION GENERAL NOTES
SHEET C3.1 ...FOUNDATION PLAN
SHEET C3.2 ...FOUNDATION DETAILS
SHEET C3.3 ...POST TENSION DETAILS
SHEET C4.0 ...PAVING DETAILS
SHEET C5.0 ...EROSION CONTROL PLAN
SHEET C5.1 ...EROSION CONTROL DETAILS
SHEET C6.0 ...SWPPP NARRATIVE PLAN
SHEET E-1 ... SITE PLAN-ELECTRICAL
SHEET E-2 ... ELECTRICAL DETAILS &SCHEDULES
SHEET E-3 ... ELECTRICAL SPECIFICATION

EXHIBIT 'D'



CITY OF FRISCO PURCHASING DIVISION

March 2, 2010

**Addendum #1
Bid # 1002-033
PRESTON PARK NORTH**

CLARIFICATION

Bids must be received by 03/09/10 at 2:00 pm by the purchasing manager's office

MODIFICATION TO SCOPE OF WORK

All Irrigation controllers will be temporary controllers as shown on enclosed addendum #1 irrigation drawings (L7.0 and L7.2)

Additional changes as clouded on enclosed addendum #1 Irrigation drawings sheets L7.0 and L7.2

DELETION TO BID FORM

Line item C 13. Controller (48sta) shall be deleted as it is not needed. City will provide permanent controller upon completion of the project. Contractor will provide temporary controllers, which will be removed by the contractor upon city acceptance of the job.



Acknowledgement of Addenda: #1 ____ #2 ____ #3 ____ #4 ____ #5 ____

Vendors who may have already submitted a bid and feel this addendum may change their bid price, may pick up their bid, and return it by the closing date. If picking up the bid is not feasible, any new bid submitted by your firm will supersede one previously submitted.

Acknowledge receipt of this addendum by initialing in the appropriate space on the bid document.

Sincerely,

Jean Stellatella
Buyer
City of Frisco

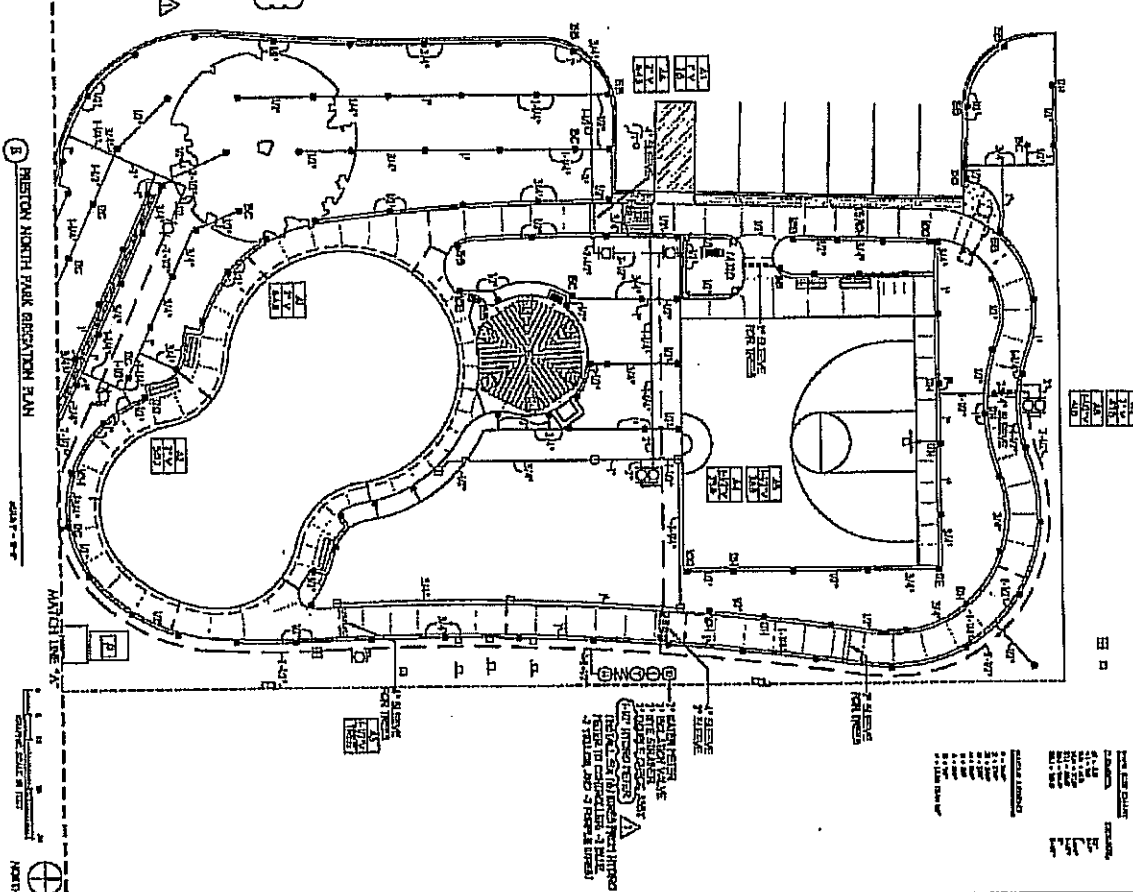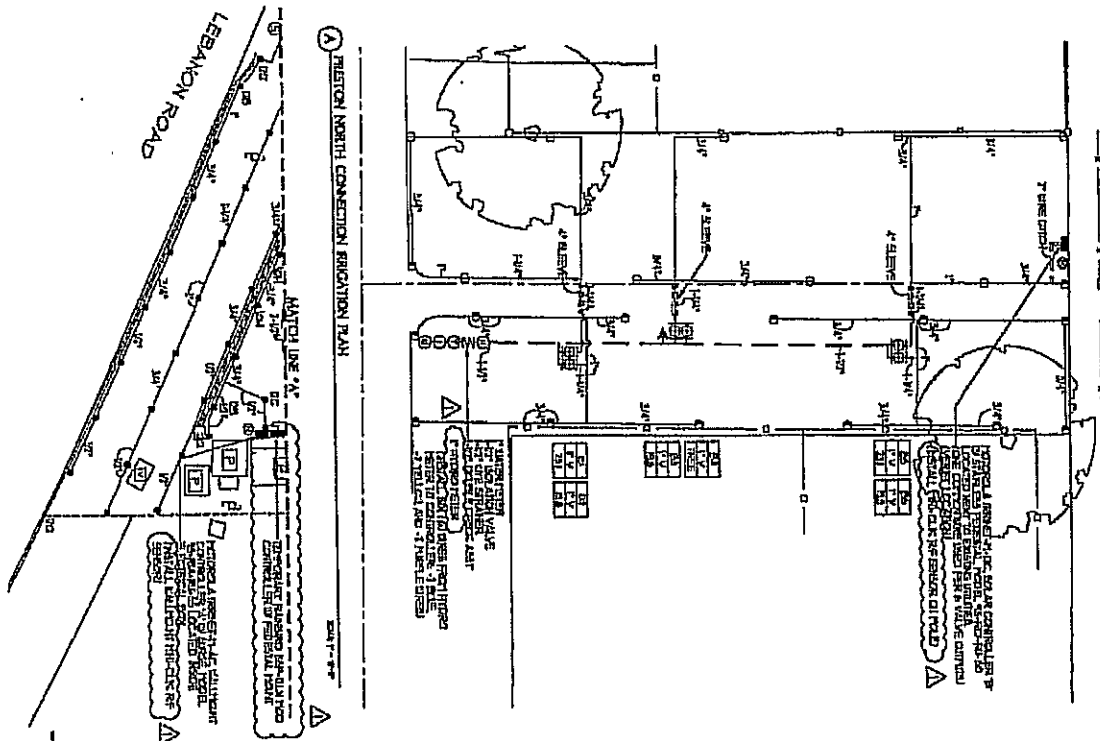


Legend

1. IRRIGATION CANAL	2. IRRIGATION CANAL
3. IRRIGATION CANAL	4. IRRIGATION CANAL
5. IRRIGATION CANAL	6. IRRIGATION CANAL
7. IRRIGATION CANAL	8. IRRIGATION CANAL
9. IRRIGATION CANAL	10. IRRIGATION CANAL
11. IRRIGATION CANAL	12. IRRIGATION CANAL
13. IRRIGATION CANAL	14. IRRIGATION CANAL
15. IRRIGATION CANAL	16. IRRIGATION CANAL
17. IRRIGATION CANAL	18. IRRIGATION CANAL
19. IRRIGATION CANAL	20. IRRIGATION CANAL
21. IRRIGATION CANAL	22. IRRIGATION CANAL
23. IRRIGATION CANAL	24. IRRIGATION CANAL
25. IRRIGATION CANAL	26. IRRIGATION CANAL
27. IRRIGATION CANAL	28. IRRIGATION CANAL
29. IRRIGATION CANAL	30. IRRIGATION CANAL
31. IRRIGATION CANAL	32. IRRIGATION CANAL
33. IRRIGATION CANAL	34. IRRIGATION CANAL
35. IRRIGATION CANAL	36. IRRIGATION CANAL
37. IRRIGATION CANAL	38. IRRIGATION CANAL
39. IRRIGATION CANAL	40. IRRIGATION CANAL
41. IRRIGATION CANAL	42. IRRIGATION CANAL
43. IRRIGATION CANAL	44. IRRIGATION CANAL
45. IRRIGATION CANAL	46. IRRIGATION CANAL
47. IRRIGATION CANAL	48. IRRIGATION CANAL
49. IRRIGATION CANAL	50. IRRIGATION CANAL
51. IRRIGATION CANAL	52. IRRIGATION CANAL
53. IRRIGATION CANAL	54. IRRIGATION CANAL
55. IRRIGATION CANAL	56. IRRIGATION CANAL
57. IRRIGATION CANAL	58. IRRIGATION CANAL
59. IRRIGATION CANAL	60. IRRIGATION CANAL
61. IRRIGATION CANAL	62. IRRIGATION CANAL
63. IRRIGATION CANAL	64. IRRIGATION CANAL
65. IRRIGATION CANAL	66. IRRIGATION CANAL
67. IRRIGATION CANAL	68. IRRIGATION CANAL
69. IRRIGATION CANAL	70. IRRIGATION CANAL
71. IRRIGATION CANAL	72. IRRIGATION CANAL
73. IRRIGATION CANAL	74. IRRIGATION CANAL
75. IRRIGATION CANAL	76. IRRIGATION CANAL
77. IRRIGATION CANAL	78. IRRIGATION CANAL
79. IRRIGATION CANAL	80. IRRIGATION CANAL
81. IRRIGATION CANAL	82. IRRIGATION CANAL
83. IRRIGATION CANAL	84. IRRIGATION CANAL
85. IRRIGATION CANAL	86. IRRIGATION CANAL
87. IRRIGATION CANAL	88. IRRIGATION CANAL
89. IRRIGATION CANAL	90. IRRIGATION CANAL
91. IRRIGATION CANAL	92. IRRIGATION CANAL
93. IRRIGATION CANAL	94. IRRIGATION CANAL
95. IRRIGATION CANAL	96. IRRIGATION CANAL
97. IRRIGATION CANAL	98. IRRIGATION CANAL
99. IRRIGATION CANAL	100. IRRIGATION CANAL

PRESTON PARK NORTH
FRISCO, TEXAS

PREPARED BY:
J. L. WATKINS
J. L. WATKINS & ASSOCIATES
10000 N. DALLAS STREET
DALLAS, TEXAS 75243
PHONE: 214-343-1111
FAX: 214-343-1112
WWW: WWW.JLWATKINS.COM





1. The building is a three-story structure, with the first floor being the main entrance level. The second floor is the main office level, and the third floor is the main storage level. The building is located on the corner of Preston Park North and Frisco, Texas.

2. The building is a three-story structure, with the first floor being the main entrance level. The second floor is the main office level, and the third floor is the main storage level. The building is located on the corner of Preston Park North and Frisco, Texas.

3. The building is a three-story structure, with the first floor being the main entrance level. The second floor is the main office level, and the third floor is the main storage level. The building is located on the corner of Preston Park North and Frisco, Texas.

4. The building is a three-story structure, with the first floor being the main entrance level. The second floor is the main office level, and the third floor is the main storage level. The building is located on the corner of Preston Park North and Frisco, Texas.

5. The building is a three-story structure, with the first floor being the main entrance level. The second floor is the main office level, and the third floor is the main storage level. The building is located on the corner of Preston Park North and Frisco, Texas.

6. The building is a three-story structure, with the first floor being the main entrance level. The second floor is the main office level, and the third floor is the main storage level. The building is located on the corner of Preston Park North and Frisco, Texas.

7. The building is a three-story structure, with the first floor being the main entrance level. The second floor is the main office level, and the third floor is the main storage level. The building is located on the corner of Preston Park North and Frisco, Texas.

8. The building is a three-story structure, with the first floor being the main entrance level. The second floor is the main office level, and the third floor is the main storage level. The building is located on the corner of Preston Park North and Frisco, Texas.

9. The building is a three-story structure, with the first floor being the main entrance level. The second floor is the main office level, and the third floor is the main storage level. The building is located on the corner of Preston Park North and Frisco, Texas.

10. The building is a three-story structure, with the first floor being the main entrance level. The second floor is the main office level, and the third floor is the main storage level. The building is located on the corner of Preston Park North and Frisco, Texas.
